


# Work Complete:

- POD A Reconstruction
- POD B Reconstruction
- POD G Reconstruction
- POD H Reconstruction
- POD I Reconstruction
- POD K Reconstruction



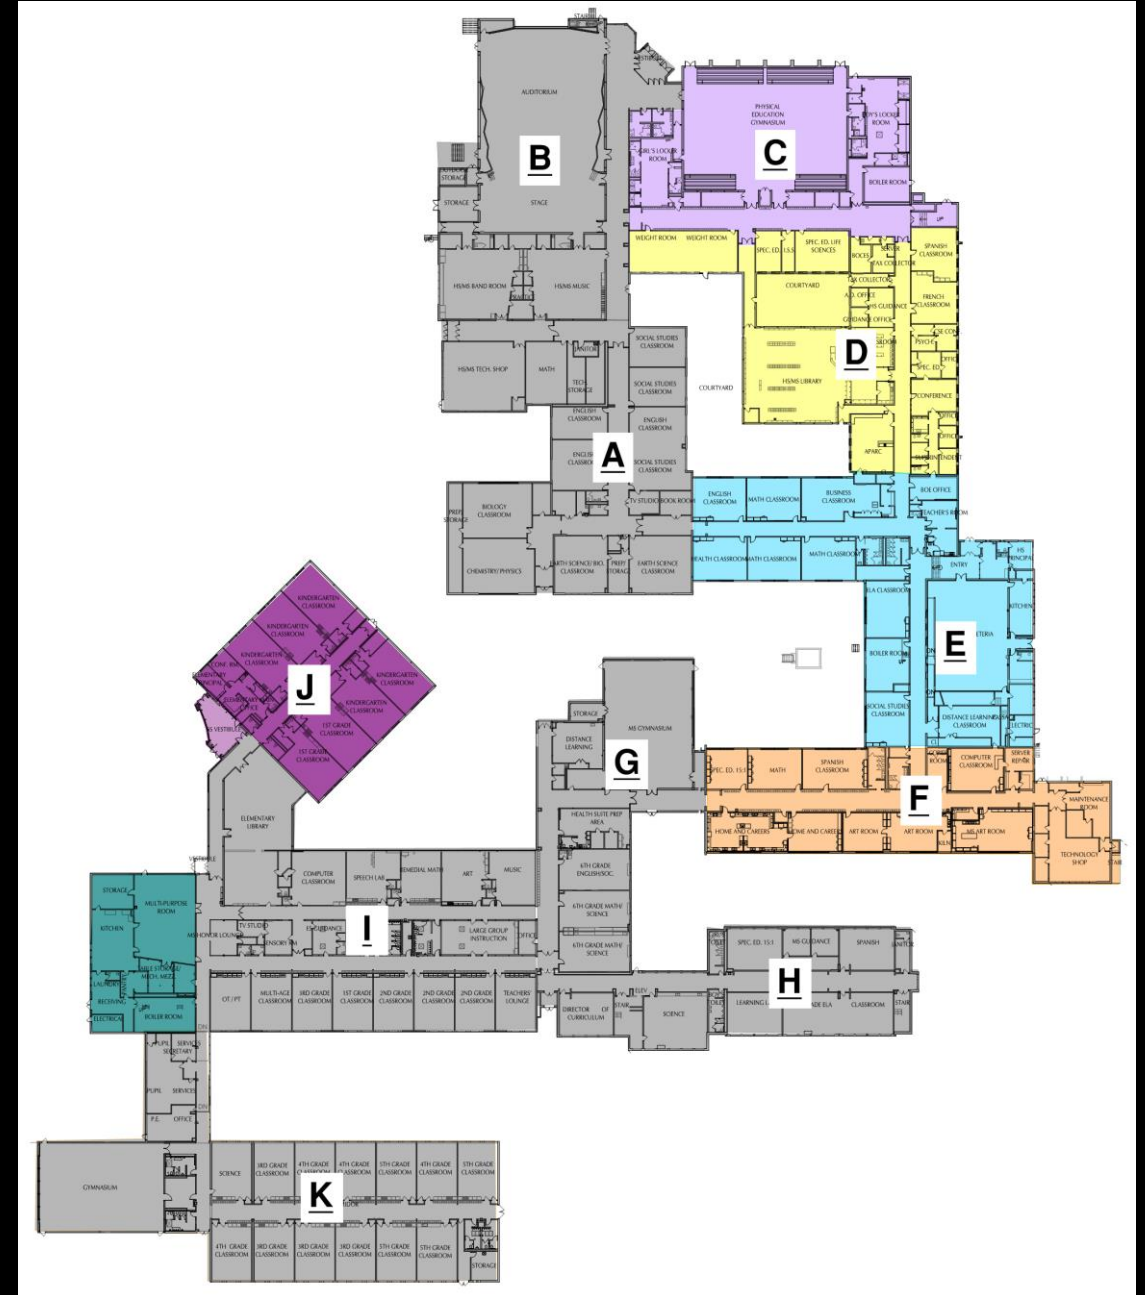

POD I Reconstruction  
Completed 04/25/2019





POD G Reconstruction  
Completed 04/05/2019



POD H Reconstruction  
Completed 04/05/2019

POD A Reconstruction  
Completed 05/31/2019






# Summer 2019 Update

## Remaining Work:

- **POD C Reconstruction**
  - Anticipated Completion: 08/23/19
- **POD D Reconstruction**
  - Anticipated Completion: 08/15/2019
- **POD E Reconstruction**
  - Anticipated Completion: 09/13/19
- **POD F Reconstruction**
  - Anticipated Completion: 09/13/19
- **POD I Kitchen Reconstruction**
  - Anticipated Completion: 08/30/19
- **POD J Reconstruction**
  - Anticipated Completion: 08/30/19
- **ES Site Work**
  - Anticipated Completion: 08/30/19

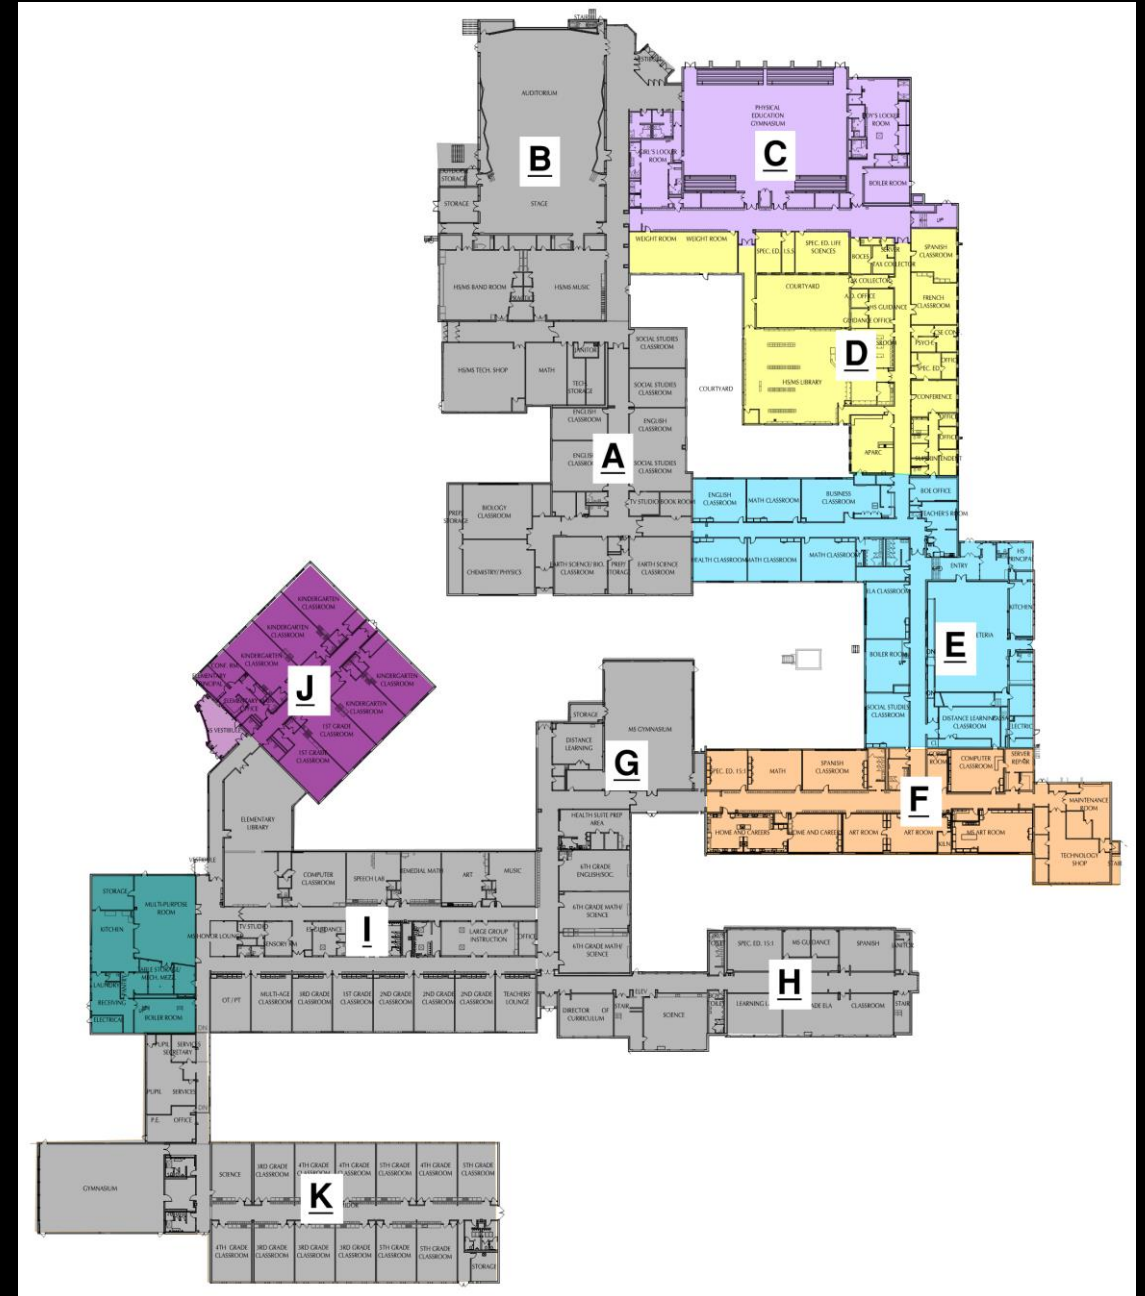



POD C HS GYM DEMO



POD J VESTIBULE &  
OFFICE







Tennis Courts  
& Basketball  
Courts



# Summer 2019 Update

## Contractor Billing:

Previous Billings	Current Billing	Total to Date
April 2019	May 2019	Thru May 2019
\$1,057,618.61	\$1,281,002.76	\$15,972,202.12
Project Percent Complete		75%

