

Schedule Milestones

Description	Original Start	Revised/ Actual	Original Completion	Revised/ Actual
Mobilize	5/28/2018	06/07/2018	09/30/2019	
HS Site	5/28/2018	06/11/2018	09/30/2019	
POD K	07/02/2018	07/02/2018	12/28/2018	12/21/2018
POD B Auditorium	07/02/2018	06/25/2018	01/20/2019	01/20/2019
POD B Music Rooms	07/02/2018	06/25/2018	01/20/2019	12/28/2018
POD I Multipurpose	06/25/2018	07/05/2018	08/17/2018	08/31/2018
POD J Addition	08/20/2018	09/04/2018	12/21/2018	
POD I Classrooms	12/24/2018	12/21/2018	06/28/2019	04/26/2019
POD I Kitchen	06/24/2019		08/30/2019	
POD A	01/02/2019	03/04/2019	06/28/2019	
POD G	01/02/2019	12/21/2018	04/05/2019	04/05/2019
POD H	01/02/2019	01/07/2019	04/05/2019	04/05/2019
POD D	04/08/2019	04/01/2019	08/15/2019	
POD E	04/15/2019	04/01/2019	09/13/2019	
POD F	04/15/2019	04/19/2019	09/13/2019	
POD C	06/03/2019	06/05/2019	08/23/2019	
POD J Classrooms	06/24/2019		08/30/2019	
ES Site	06/24/2019	06/03/2019	08/30/2019	
Old Bus Garage Demo	06/04/2018	06/07/2018	07/27/2018	06/28/2018
Comments: Schedule Update 06/15/2019				

Prime Contractors:

- 1) Sullivan Contracting—Abatement Contractor (AC)
- 2) HMA Contracting—Site Contractor (SC)
- 3) Bast Hatfield Construction —General Contractor (GC)
- 4) DiGesare Mechanical—Mechanical Contractor (MC)
- 5) Clune Electric—Electrical Contractor (EC)
- 6) Tri-Valley Plumbing —Plumbing Contractor (PC)
- 7) Titan Roofing—Roofing Contractor (RC)
- 8) TBS Controls—Controls Contractor (CC)

Project Update:

Overall Roof Work 95% Complete

HS Site Work 95% Complete | ES Site Work In Progress

Complete PODS:

- POD B: Punch List 95% Complete
- POD G: Punch List 95% Complete
- POD H: Punch List 95% Complete
- POD I: Punch List 85% Complete (Excluding Kitchen)
- POD K: Punch List 95% Complete

PODS IN PROGRESS:

POD A: (Reconstruction Phase)

- Mechanical Work: New Units 100% Installed
- Architectural Renovations: 90% Complete
 - ◊ Ceiling work On-Going
- Plumbing Work: 80% Complete
 - ◊ Water Fountain installation On-Going
- Electrical Work: 100% Complete

POD C: (Demo Phase)

- HS Gym Floor Abatement & Demo On-Going
- Mechanical/Architectural Demo 75% Complete

POD D: (Demo Phase)

- Mechanical/Architectural Demo 60% Complete

POD E: (Demo & Reconstruction Phase)

- Mechanical/Architectural Demo 90% Complete
- Architectural Renovations: 15% Complete
 - ◊ Classroom Flooring and Painting On-Going

POD F: (Reconstruction Phase)

- Mechanical Work: New Units 90% Installed
- Architectural Renovations: 65% Complete
 - ◊ Sheetrocking & Taping On-Going
- Plumbing Work: 70% Complete
 - ◊ Home & Careers and Art Room Sinks 100% Roughed In

POD J: (Demo and Reconstruction Phase)



- Architectural Renovations: 65% Complete
 - ◊ Sheetrock & Taping On-Going in Office and Vestibule
- Mechanical Work: Demo 15% Complete, New Units 10% Installed


Project Constraints

Constraint	Impact	Status
Weather	Site Work and Roofing Work Limited	On-Going
Existing Building Components	Unforeseen Cost and Schedule Impacts	On-Going

Engineering Status

Requests for Information			
Total RFIs	Closed RFIs	Open RFIs	Overdue RFIs
272	265	7	0
Submittals			
Open Items	Closed Items	In Review	Overdue
89	388	2	2
TOTAL:	479	% Closed:	81%

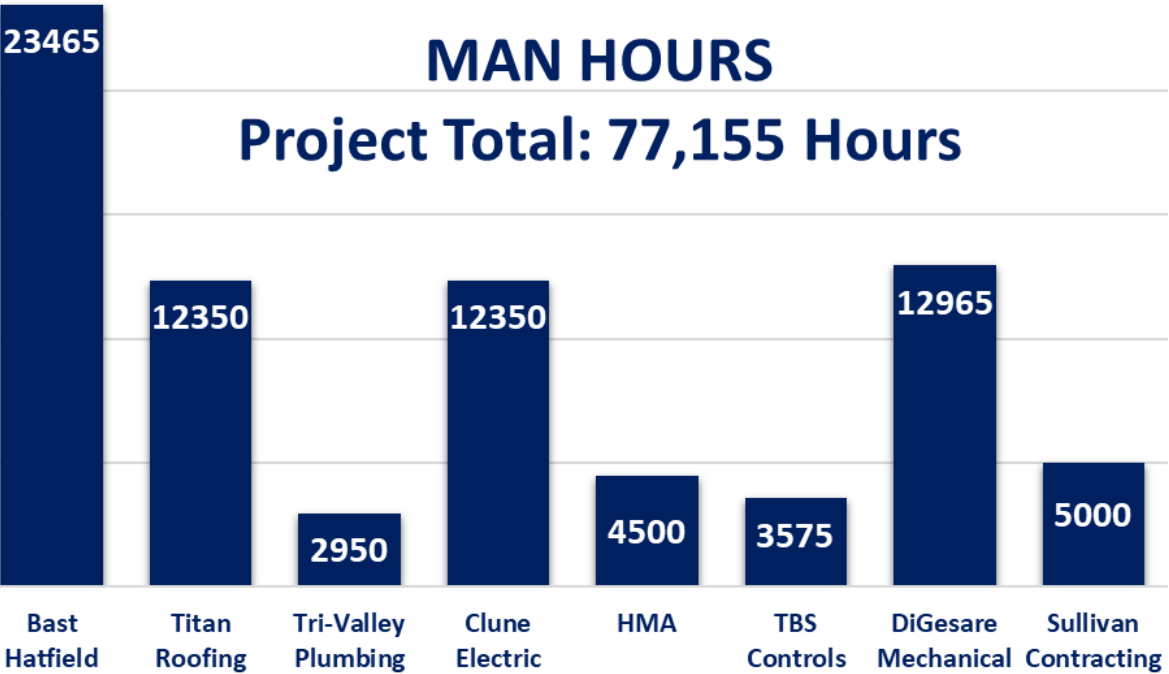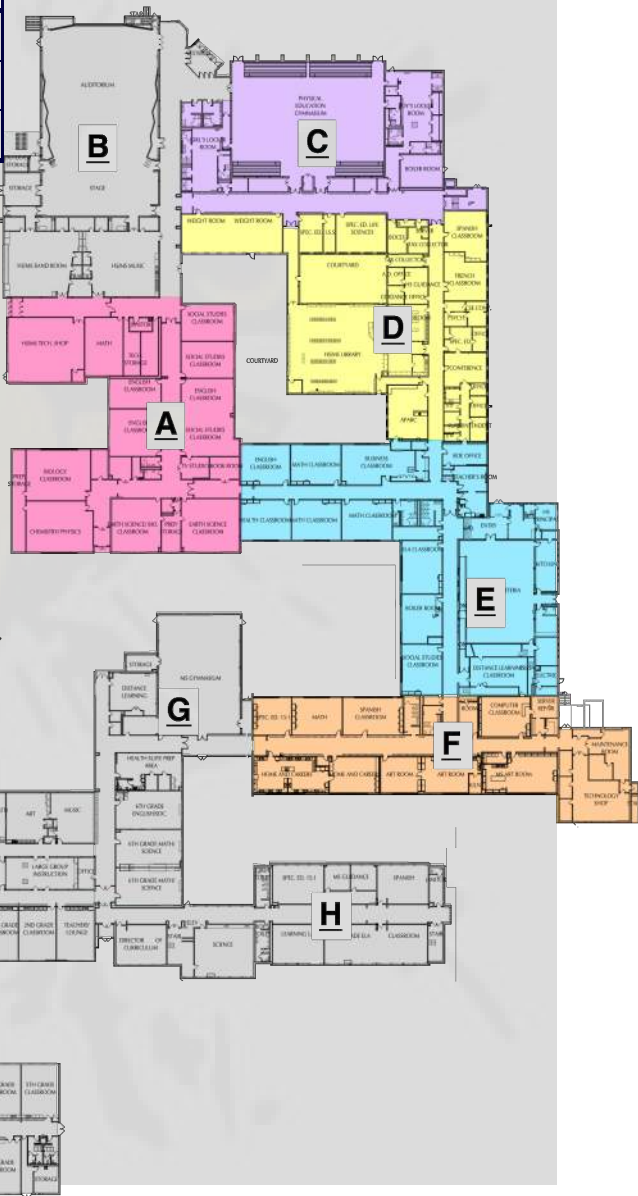

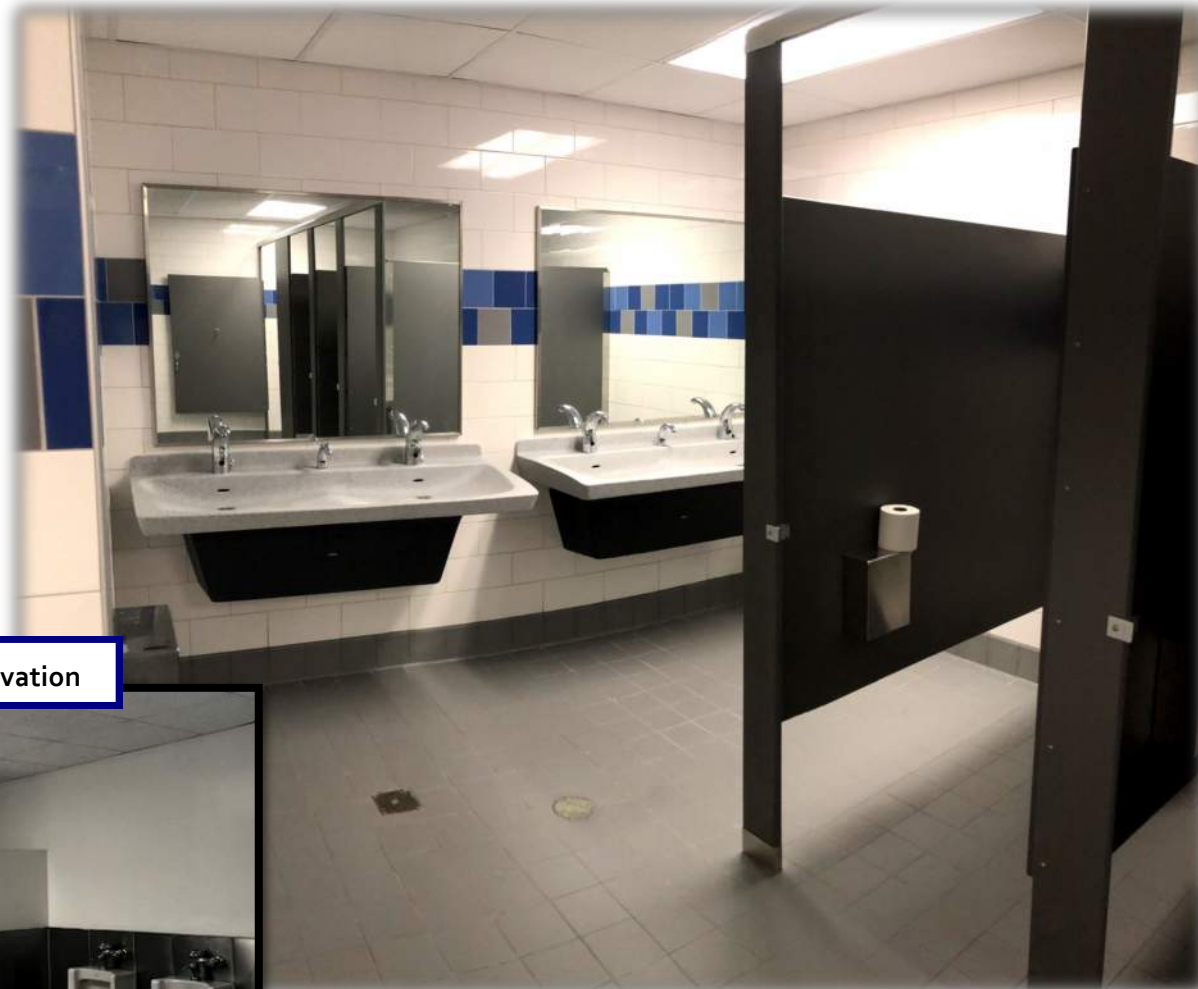

Bathroom Renovation



"Fishbowl" Renovation



Classroom Renovation



Galway CSD Capital
Improvement Project
Executive Summary
BOE Update 6.20.19

POD I Renovation

CSARCH **Turner**
Construction Company



POD J VESTIBULE & OFFICE



TENNIS & BASKETBALL COURTS



HS GYM FLOOR DEMO



Galway CSD Capital
Improvement Project
Executive Summary
BOE Update 6.20.19

PROGRESS PHOTOS
CSARCH **Turner**
Construction Company
