

Prime Contractors:

- 1) Sullivan Contracting—Abatement Contractor (AC)
- 2) HMA Contracting—Site Contractor (SC)
- 3) Bast Hatfield Construction —General Contractor (GC)
- 4) DiGesare Mechanical—Mechanical Contractor (MC)
- 5) Clune Electric—Electrical Contractor (EC)
- 6) Tri-Valley Plumbing —Plumbing Contractor (PC)
- 7) Titan Roofing—Roofing Contractor (RC)
- 8) TBS Controls—Controls Contractor (CC)

Project Update:

⇒ Roofing Work Substantially Complete

⇒ High School Site: *Punch list On-Going*

- ◆ Finished Pavement & Striping Completed

⇒ Elementary School Site:

- ◆ Parking Lot Final Grading Complete
- ◆ Sidewalk Installation Throughout
- ◆ Parking Lot Paving & Striping Complete
- ◆ Site Restoration On-Going

⇒ POD C Work Progressing:

- ◆ HS Gym Floor Subbase & Hardwood Installed
- ◆ HS Gym Floor Sealed & Game Striping Applied
- ◆ Corridor Ceilings Installed
- ◆ Mechanical Work Complete
- ◆ Door & Hardware Installation

⇒ POD J Work Progressing:

- ◆ Mechanical Units Installed & Work Complete
- ◆ Terrazzo Floor & Base Installation Complete
- ◆ Vestibule Light Installation
- ◆ Main Office Casework Installation

⇒ POD E Work Progressing:

- ◆ HS Cafeteria Framing/Sheetrock & Painting
- ◆ HS Cafeteria Decorative Panel Installation
- ◆ Boiler Room & Crawl Space Mechanical Work On-Going
- ◆ Kitchen Equipment Set & Plumbing Installed
- ◆ Classroom Casework Installation
- ◆ Faculty Room Paint/Ceilings & Casework

⇒ POD D Work Progressing:

- ◆ Mechanical Work Complete
- ◆ District Office Ceiling Installation
- ◆ Door & Hardware Installation
- ◆ Corridor Ceiling Installation

⇒ POD F Work Progressing:

- ◆ Home & Careers/Art Rooms Paint & Ceilings
- ◆ Art Room Storefront Installed
- ◆ Computer Room Paint & Ceiling
- ◆ Flooring Installed Throughout
- ◆ Corridor Ceiling Installation
- ◆ Casework Installation Throughout

⇒ POD I Kitchen:

- ◆ Kitchen Equipment Set & Plumbing Installed
- ◆ Ansul Fire Suppression System Certified

We would like to thank the District for their continued flexibility and positivity throughout the past 16 months of construction. This project would not have been a success without the help of all involved. The Construction team looks forward to wrapping up the final details.

Galway CSD Capital Improvement Project Executive Summary August 2019

Schedule Milestones

Description	Original Start	Revised/ Actual	Original Completion	Revised/ Actual
Mobilize	5/28/2018	06/07/2018	09/30/2019	
HS Site	5/28/2018	06/11/2018	09/30/2019	08/26/2019
POD K	07/02/2018	07/02/2018	12/28/2018	12/21/2018
POD B Auditorium	07/02/2018	06/25/2018	01/20/2019	01/20/2019
POD B Music Rooms	07/02/2018	06/25/2018	01/20/2019	12/28/2018
POD I Multipurpose	06/25/2018	07/05/2018	08/17/2018	08/31/2018
POD J Addition	08/20/2018	09/04/2018	12/21/2018	08/30/2019
POD I Classrooms	12/24/2018	12/21/2018	06/28/2019	04/26/2019
POD I Kitchen	06/24/2019	06/26/2019	08/30/2019	08/23/2019
POD A	01/02/2019	03/04/2019	06/28/2019	06/24/2019
POD G	01/02/2019	12/21/2018	04/05/2019	04/05/2019
POD H	01/02/2019	01/07/2019	04/05/2019	04/05/2019
POD D	04/08/2019	04/01/2019	08/15/2019	08/30/2019
POD E	04/15/2019	04/01/2019	09/13/2019	08/30/2019
POD E MS Boiler Room	04/30/2019	04/30/2019	09/13/2019	
POD F	04/15/2019	04/19/2019	09/13/2019	08/30/2019
POD C	06/03/2019	06/05/2019	08/23/2019	08/30/2019
POD J Classrooms	06/24/2019	06/26/2019	08/30/2019	08/30/2019
ES Site	06/24/2019	07/01/2019	08/30/2019	08/30/2019
Old Bus Garage Demo	06/04/2018	06/07/2018	07/27/2018	06/28/2018
Comments: Schedule Update 08/31/2019				

Field Reports / Inspections


Inspections performed	Date Issued	Status
Dente Group—SWPPP	On-Going	Weekly
Architectural Punch List POD K	12.28.18	In-Progress
Architectural Punch List POD B	01.24.19	In-Progress
Architectural Punch List POD I	05.16.19	In-Progress
Architectural Punch List POD A	06.08.19	In-Progress
High School Site Punch List	07.09.19	In-Progress
Architectural Punch List POD J	08.30.19	In-Progress
Mechanical Punch List All PODs	08.30.19	In-Progress



08/01/2019 - 08/31/2019

Man Hours: 10,218

Project Total: 100,255 Hours

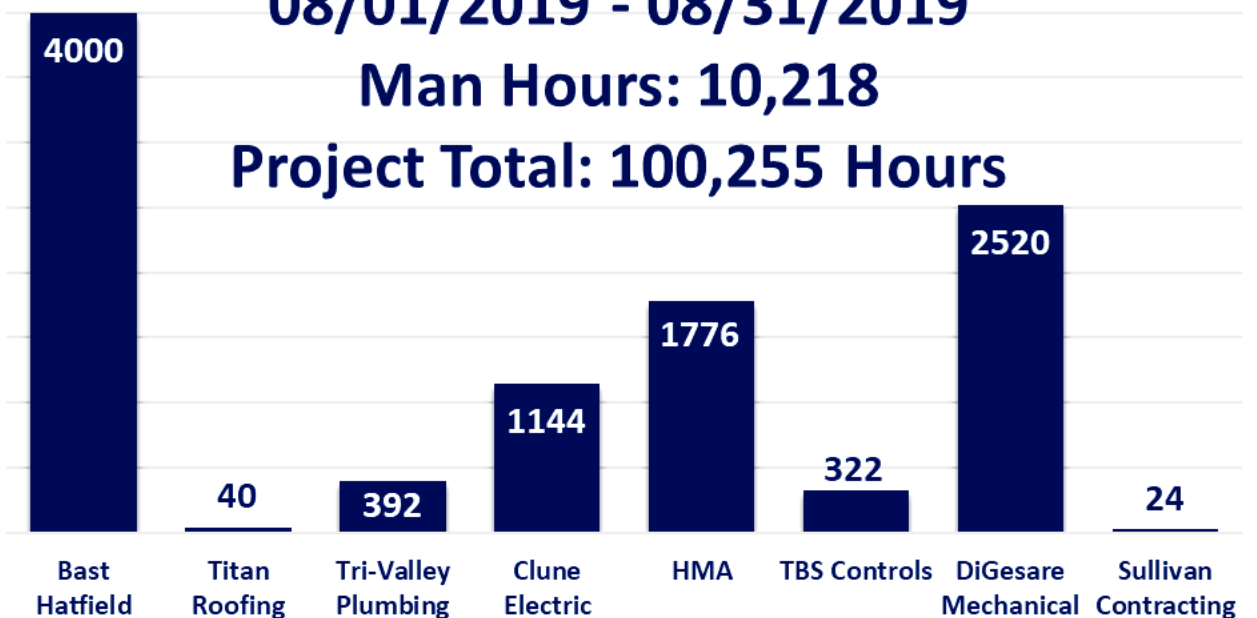

Engineering Status


Requests for Information			
Total RFIs	Closed RFIs	Open RFIs	Overdue RFIs
295	294	1	1
Submittals			
Open Items	Closed Items	In Review	Overdue
11	395	1	0
TOTAL:	406	% Closed:	97%

Closeout Status

Status	Open Items	% Complete	Challenges
On-Going	174/221	21%	N/A

Contractor Billings

Previous Billings	Current Billing	Total to Date
July 2019	Aug 2019	Through Aug 2019
\$1,764,559.51	\$1,755,268.32	\$20,385,129.79
Project % Complete:		95.00%

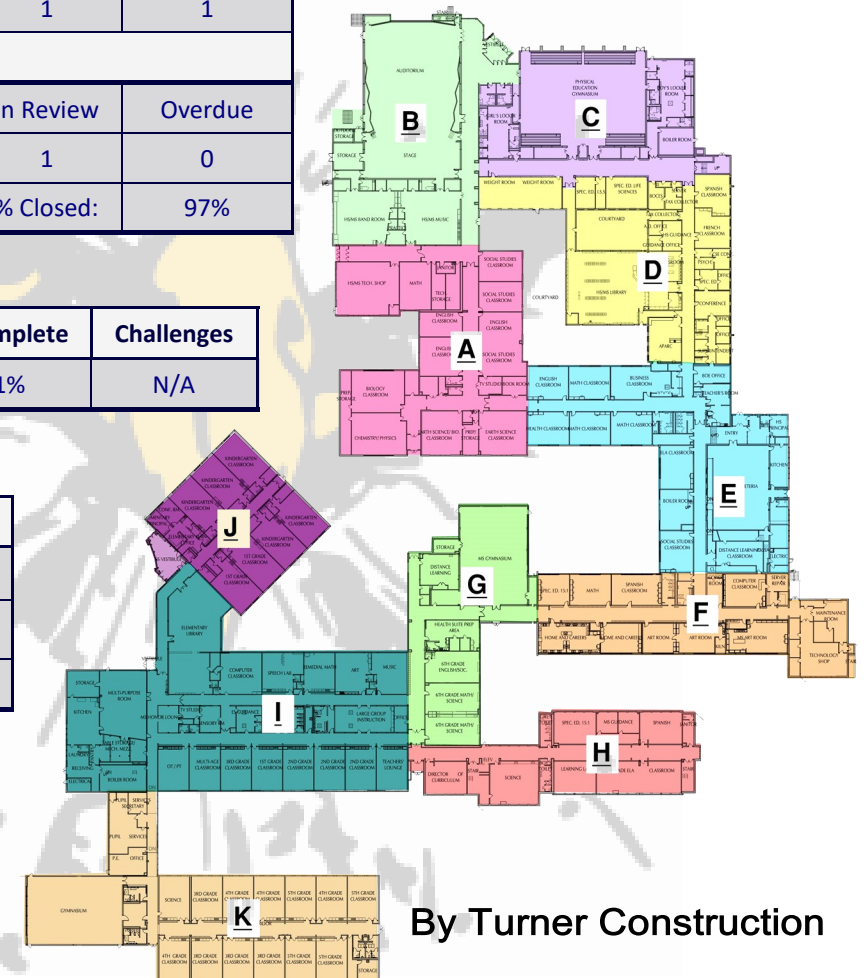

By Turner Construction

Galway CSD Capital Improvement Project
Executive Summary August 2019

Turner
Construction Company

CS**ARCH**



**HS/ES Site Work & Secure
Entrance Vestibule**



POD F Computer Rm



POD E Classroom



POD F Home & Careers



HS Cafeteria



POD J ES Main Office



POD C HS Gym



POD J ES Vestibule



POD D APARC



Galway CSD Capital Improvement Project
Executive Summary August 2019

Turner
Construction Company

CSARCH
