

Prime Contractors:

- 1) Sullivan Contracting—Abatement Contractor (AC)
- 2) HMA Contracting—Site Contractor (SC)
- 3) Bast Hatfield Construction —General Contractor (GC)
- 4) DiGesare Mechanical—Mechanical Contractor (MC)
- 5) Clune Electric—Electrical Contractor (EC)
- 6) Tri-Valley Plumbing —Plumbing Contractor (PC)
- 7) Titan Roofing—Roofing Contractor (RC)
- 8) TBS Controls—Controls Contractor (CC)

Project Update:

- ⇒ Roofing Work Progressing: 80% Complete.

◆ Fascia installation throughout

◆ POD J Addition Roof Installed
- ⇒ High School Site Work progressing:

◆ Student Parking Lot Paved (Binder Only)

◆ Student Parking Lot Striped and Numbered

◆ Site Stabilized for Winter Months
- ⇒ POD K Work progressing:

◆ Installation of new mechanical equipment & controls

◆ Continued install of exterior wall at ES Gym

◆ Installation of framing and sills for windows at ES Gym

◆ Finishes On-Going:

◆ Bathroom Wall and Floor Tile

◆ Classroom Ceilings

◆ Classroom Floors

◆ ES Gym Ceiling & Wall Paint

◆ Bathroom Fixtures

◆ Corridor Ceilings
- ⇒ POD B Work progressing:

◆ New exterior stair installation continued

◆ Music Room Soffit Paint

◆ Music Room Ceiling Grid installation

◆ Mechanical equipment installed throughout

◆ Installation of new electrical wiring/equipment

◆ Replacement of Audio/Visual System 90%

◆ Auditorium Projector Installed

◆ Aisle Lighting Installation On-Going

◆ Partial Replacement of Stage Completed

◆ Stage Refinished and Painted

◆ Auditorium Seating Installed

◆ Auditorium/Stage Wall Paint Complete
- ⇒ POD J Addition Work Progressing:

◆ Vestibule Slab Poured

With the installation of finishes ongoing we look forward to the substantial completion of POD K and the Music Rooms next month. We continue to thank the District on their willingness to work with us and the construction team. Extensive coordination and communication will allow for a smooth transition into the next phases of the project in January.

Schedule Milestones

Description	Original Start	Revised/ Actual	Original Completion	Revised/ Actual
Mobilize	5/28/2018	6/7/2018		
HS Site	5/28/2018	6/11/2018	9/30/2019	
POD K	7/2/2018	7/2/2018	12/28/2018	
POD B	7/2/2018	6/25/2018	1/20/2019	
POD I Multipurpose	6/25/2018	7/5/2018	8/17/2018	8/31/2018
POD J Addition	8/20/2018	9/4/2018	12/21/2018	
POD I Kitchen/Classrooms	12/24/2018		6/28/2019	
POD A	1/2/2019		6/28/2019	
POD G	1/2/2019		4/5/2019	
POD H	1/2/2019		4/5/2019	
POD D	4/8/2019		8/15/2019	
POD E	4/15/2019		9/13/2019	
POD F	4/15/2019		9/13/2019	
POD C	6/3/2019		8/23/2019	
POD J Classrooms	6/24/2019		8/30/2019	
ES Site	6/24/2019		8/30/2019	
Old Bus Garage Demo	6/4/2018	6/7/2018	7/27/2018	6/28/2018
Comments: Schedule Update 11/30/2018				


Engineering Status

Requests for Information			
Total RFIs	Closed RFIs	Open RFIs	Overdue RFIs
142	138	4	2
Submittals			
Open Items	Closed Items	In Review	Overdue
197	353	25	24
TOTAL:	575	% Closed:	62%

Project Constraints

Constraint	Impact	Status
Weather	Site work and roofing work limited	On-Going
Existing Building Components	Extensive coordination with contractors	On-Going

November Man Hours
Total: 5,918 Hours

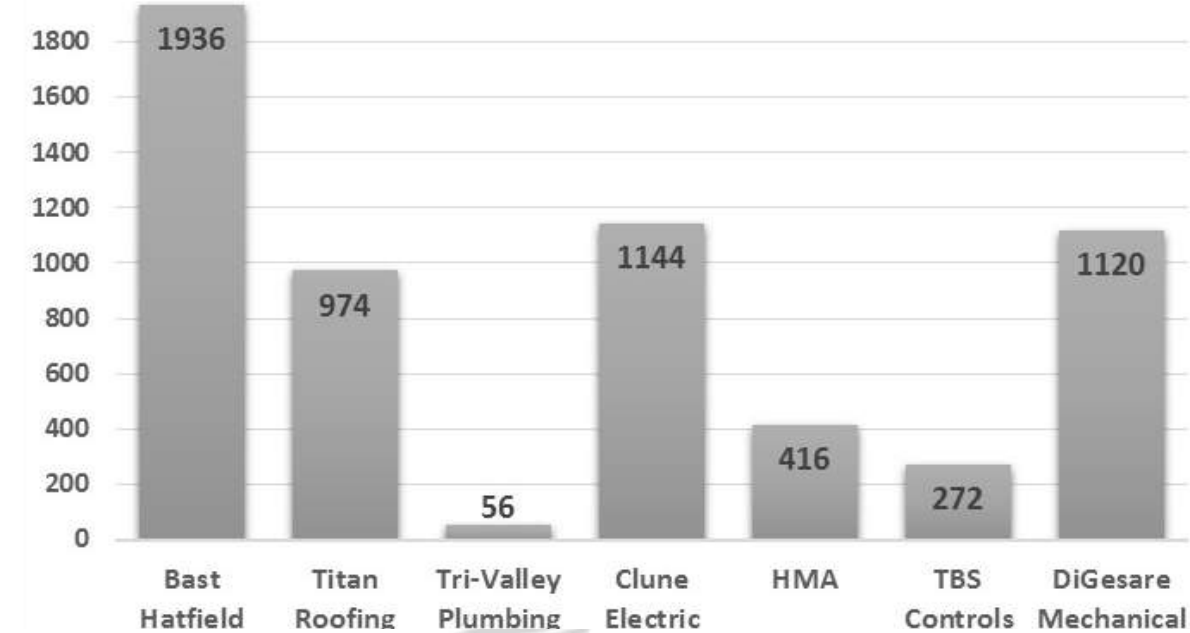


Field Reports / Inspections

Inspections performed	Date Issued	Status
Dente Group—SWPPP	On-Going	Weekly
Dente Group—Steel/Concrete	On-Going	As Necessary
PSI—Air Monitoring	On-Going	As Necessary

Project Total Man Hours: 38,652

Contractor Billings

Previous Billings	Current Billing	Total to Date
Oct 2018	Nov 2018	Thru Nov 2018
\$1,768,427.41	\$1,212,394.31	\$9,567,542.58
Project Percent Complete		44%

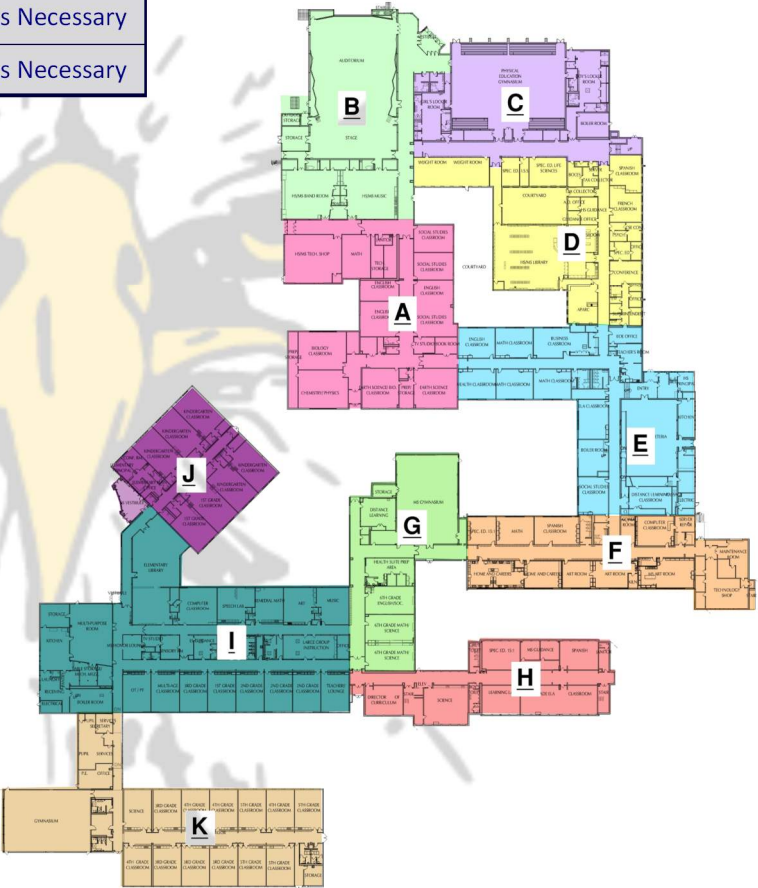



POD K Classrooms



POD K Bathrooms



HS SITE Student Parking Lot



POD B Auditorium
