


Schedule Milestones

Description	Original Start	Revised/ Actual	Original Completion	Revised/ Actual
Mobilize	5/28/2018	6/7/2018		
HS Site	5/28/2018	6/11/2018	9/30/2019	
POD K	7/2/2018	7/2/2018	12/28/2018	
POD B	7/2/2018	6/25/2018	1/20/2019	
POD I Multipurpose	6/25/2018	7/5/2018	8/17/2018	8/31/2018
POD J Addition	8/20/2018	9/4/2018	12/21/2018	
POD I Kitchen/Classrooms	12/24/2018		6/28/2019	
POD A	1/2/2019		6/28/2019	
POD G	1/2/2019		4/5/2019	
POD H	1/2/2019		4/5/2019	
POD D	4/8/2019		8/15/2019	
POD E	4/15/2019		9/13/2019	
POD F	4/15/2019		9/13/2019	
POD C	6/3/2019		8/23/2019	
POD J Classrooms	6/24/2019		8/30/2019	
ES Site	6/24/2019		8/30/2019	
Old Bus Garage Demo	6/4/2018	6/7/2018	7/27/2018	6/28/2018
Comments: Schedule Update 10/31/2018				

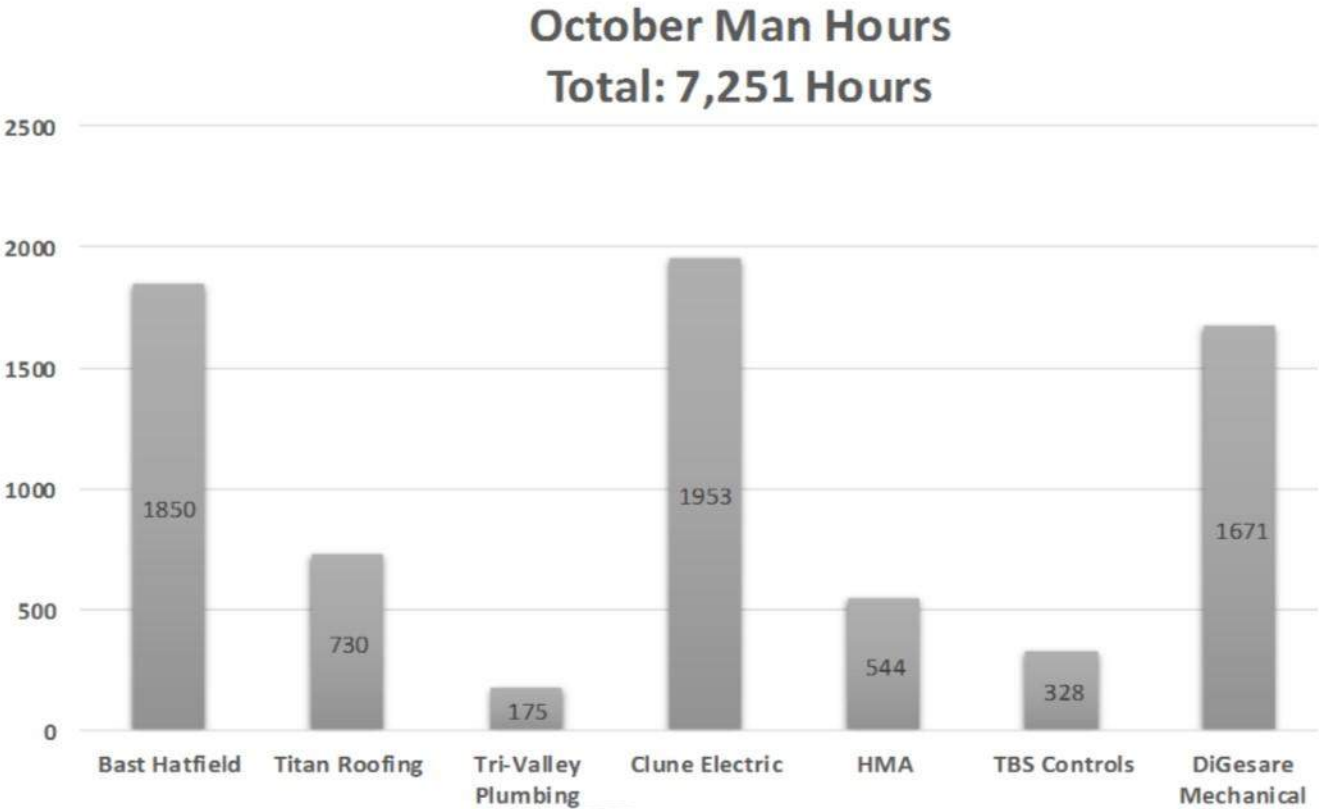

Prime Contractors:

- 1) Sullivan Contracting—Abatement Contractor (AC)
- 2) HMA Contracting—Site Contractor (SC)
- 3) Bast Hatfield Construction —General Contractor (GC)
- 4) DiGesare Mechanical—Mechanical Contractor (MC)
- 5) Clune Electric—Electrical Contractor (EC)
- 6) Tri-Valley Plumbing —Plumbing Contractor (PC)
- 7) Titan Roofing—Roofing Contractor (RC)
- 8) TBS Controls—Controls Contractor (CC)

Project Update:

- ⇒ Roofing Work Progressing: 75% Complete.
 - ◆ Reroofing of POD K Roof started
 - ◆ Fascia installation throughout
- ⇒ High School Site Work progressing:
 - ◆ Storm water detention system installed
 - ◆ Student Parking Lot Sidewalks installed
- ⇒ POD K work progressing:
 - ◆ Bathroom Framing Continued
 - ◆ Plumbing rough-in 100% complete
 - ◆ Installation of new mechanical equipment
 - ◆ Installation of new ductwork in ES Gym
 - ◆ Continued installed of exterior wall at ES Gym
 - ◆ Finishes Started:
 - ◆ Bathroom wall tile
 - ◆ Classroom ceiling and wall paint
- ⇒ POD B Work progressing:
 - ◆ New exterior stair installation continued
 - ◆ Installation of new soffits in music rooms
 - ◆ Mechanical equipment installed throughout
 - ◆ Installation of new electrical wiring/equipment
 - ◆ Auditorium lighting replaced
 - ◆ On-Going replacement of Audio/Visual System
 - ◆ Auditorium Projector Screen installed
 - ◆ New stage subbase installed
 - ◆ Auditorium ceiling and wall painting started
- ⇒ POD C Boiler Room Work Progressing:
 - ◆ New mechanical equipment installed
 - ◆ Boiler programming work started
- ⇒ POD J Addition Work Progressing:
 - ◆ Foundation walls formed and poured
 - ◆ Area backfilled and new structural steel installed
 - ◆ New steel deck installed

We appreciate the District’s willingness to work with us as a team to guarantee the continuation of a successful construction project. We look forward to bringing these PODs and the Addition closer to substantial completion in the next few months to ensure a smooth transition into the next portions of the project.

Field Reports / Inspections

Inspections performed	Date Issued	Status
Dente Group—SWPPP	On-Going	Weekly
Dente Group—Steel/Concrete	On-Going	As Necessary
PSI—Air Monitoring	On-Going	As Necessary

Project Total Man Hours: 32,734

Engineering Status


Requests for Information			
Total RFIs	Closed RFIs	Open RFIs	Overdue RFIs
130	124	6	2
Submittals			
Open Items	Closed Items	In Review	Overdue
218	335	33	25
TOTAL:	575	% Closed:	58%

Contractor Billings

Previous Billings	Current Billing	Total to Date
Sept 2018	Oct 2018	Thru Oct 2018
\$1,778,380.00	\$1,768,427.41	\$8,319,634.69
Project Percent Complete		38%

Project Constraints

Constraint	Impact	Status
Weather	Site work and roofing work limited	On-Going
Existing Building Components	Extensive coordination with contractors	On-Going

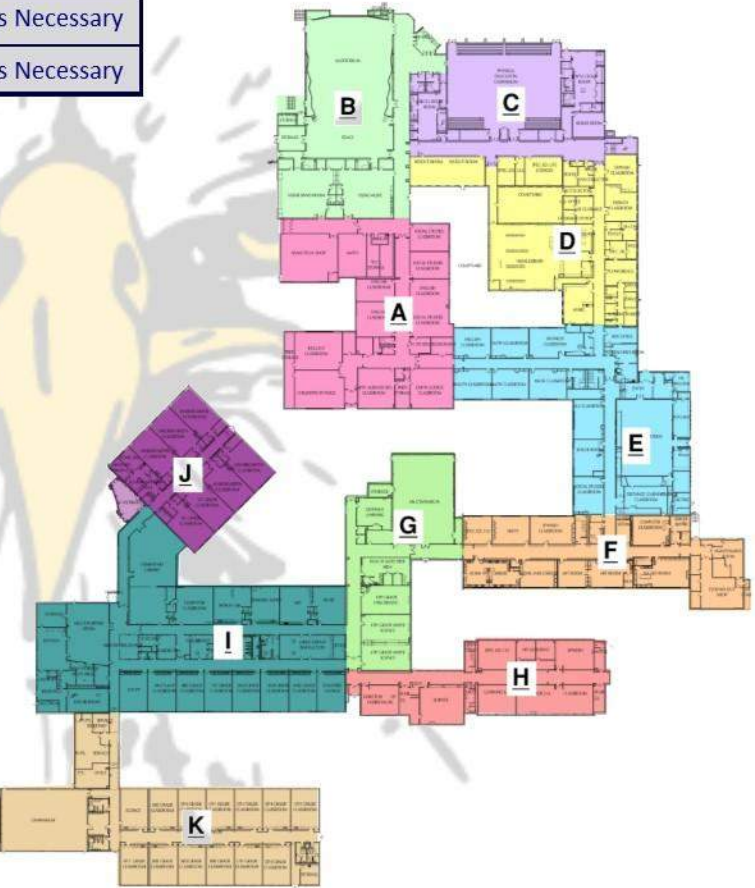



POD B Soffit and Radiant Panel Installation



HS Storm Detention System Installation



POD J Vestibule Structural Steel



POD K Roof Installation



POD B Auditorium Lights and Paint



POD K Bathroom Wall Tile



POD K Bathroom Framing
