

Prime Contractors:

- 1) Sullivan Contracting—Abatement Contractor (AC)
- 2) HMA Contracting—Site Contractor (SC)
- 3) Bast Hatfield Construction —General Contractor (GC)
- 4) DiGesare Mechanical—Mechanical Contractor (MC)
- 5) Clune Electric—Electrical Contractor (EC)
- 6) Tri-Valley Plumbing —Plumbing Contractor (PC)
- 7) Titan Roofing—Roofing Contractor (RC)
- 8) TBS Controls—Controls Contractor (CC)

Project Update:

- **September 2019 :**
 - ⇒ Middle School Boiler Room Piping
 - ⇒ Ductwork Installation
 - ⇒ Crawl Space Heating Main Installation
 - ⇒ Hallway Ceiling Tile Installation
 - ⇒ Punch List
- **October 2019 :**
 - ⇒ HS Gym Wall & Ceiling Paint
 - ⇒ Punch List
- **November 2019 :**
 - ⇒ Punch List
- **December 2019 :**
 - ⇒ Punch List

We would like to thank the District for their continued flexibility and positivity throughout the completion of the project. This project would not have been a success without the help of all involved.

Closeout Status

Status	% Complete
On-Going	96%

Engineering Status

Requests for Information			
Total RFIs	Closed RFIs	Open RFIs	Overdue RFIs
300	300	0	0
Submittals			
Open Items	Closed Items	In Review	Overdue
0	396	0	0
TOTAL:	396	% Closed:	100%

Contractor Billings

Previous Billings	Current Billing	Total to Date
Aug 2019	Sept-Dec 2019	Through Dec 2019
\$1,755,268.32	\$1,391,481.76	\$21,776,611.55
Project % Complete:		96.00%

Galway CSD Capital Improvement Project Executive Summary - January 2020

Schedule Milestones

Description	Original Start	Revised/ Actual	Original Completion	Revised/ Actual
Mobilize/Demobilize	5/28/2018	06/07/2018	09/30/2019	
HS Site	5/28/2018	06/11/2018	09/30/2019	08/26/2019
POD K	07/02/2018	07/02/2018	12/28/2018	12/21/2018
POD B Auditorium	07/02/2018	06/25/2018	01/20/2019	01/20/2019
POD B Music Rooms	07/02/2018	06/25/2018	01/20/2019	12/28/2018
POD I Multipurpose	06/25/2018	07/05/2018	08/17/2018	08/31/2018
POD J Addition	08/20/2018	09/04/2018	12/21/2018	08/30/2019
POD I Classrooms	12/24/2018	12/21/2018	06/28/2019	04/26/2019
POD I Kitchen	06/24/2019	06/26/2019	08/30/2019	08/23/2019
POD A	01/02/2019	03/04/2019	06/28/2019	06/24/2019
POD G	01/02/2019	12/21/2018	04/05/2019	04/05/2019
POD H	01/02/2019	01/07/2019	04/05/2019	04/05/2019
POD D	04/08/2019	04/01/2019	08/15/2019	08/30/2019
POD E	04/15/2019	04/01/2019	09/13/2019	08/30/2019
POD E MS Boiler Room	04/30/2019	04/30/2019	09/13/2019	10/04/2019
POD F	04/15/2019	04/19/2019	09/13/2019	08/30/2019
POD C	06/03/2019	06/05/2019	08/23/2019	08/30/2019
POD J Classrooms	06/24/2019	06/26/2019	08/30/2019	08/30/2019
ES Site	06/24/2019	07/01/2019	08/30/2019	08/30/2019
Old Bus Garage Demo	06/04/2018	06/07/2018	07/27/2018	06/28/2018
Comments: Schedule Update 01/2020				



Field Reports / Inspections

Inspections performed	Date Issued	Status
Architectural Punch List POD K	12.28.18	Complete
Architectural Punch List POD B	01.24.19	Complete
Architectural Punch List POD I	05.16.19	Complete
Architectural Punch List POD A	06.08.19	Complete
High School Site Punch List	07.09.19	Complete
Architectural Punch List POD J	08.30.19	In-Progress
Mechanical Punch List All PODs	08.30.19	Complete
Elementary School Site Punch List	09.06.19	In-Progress
Architectural Punch List POD E,F,D,C	09.20.19	In-Progress



PROJECT TOTAL MAN HOURS TO DATE:

101,610

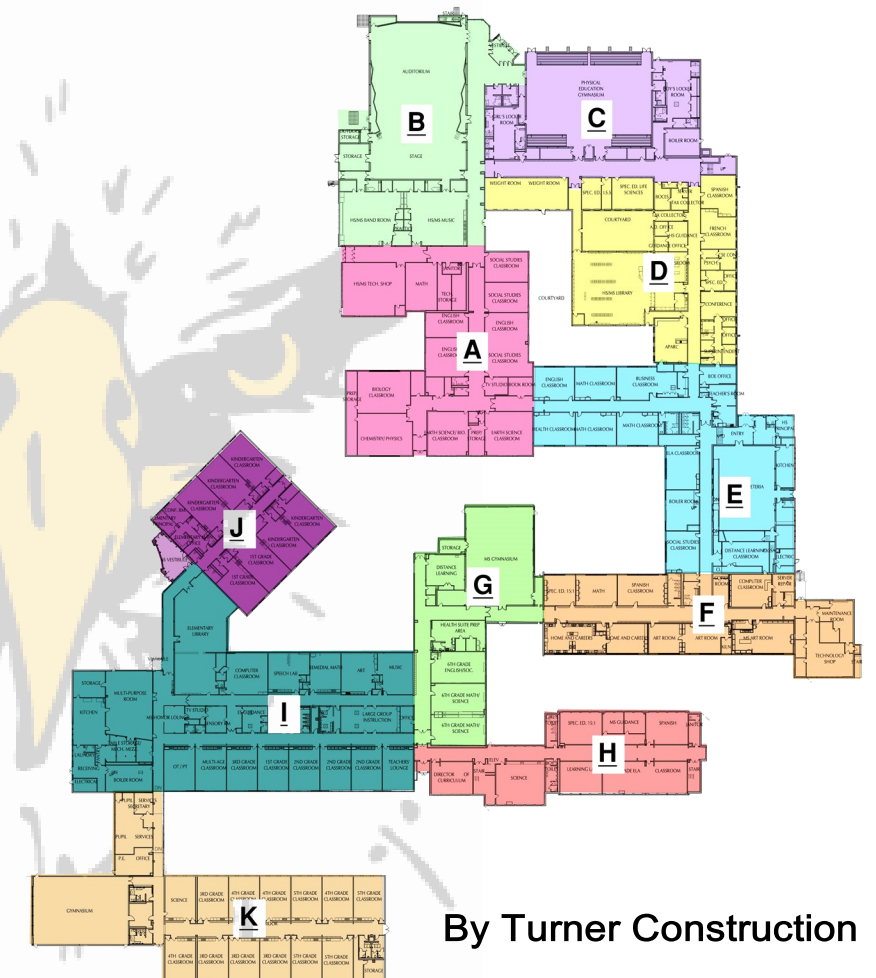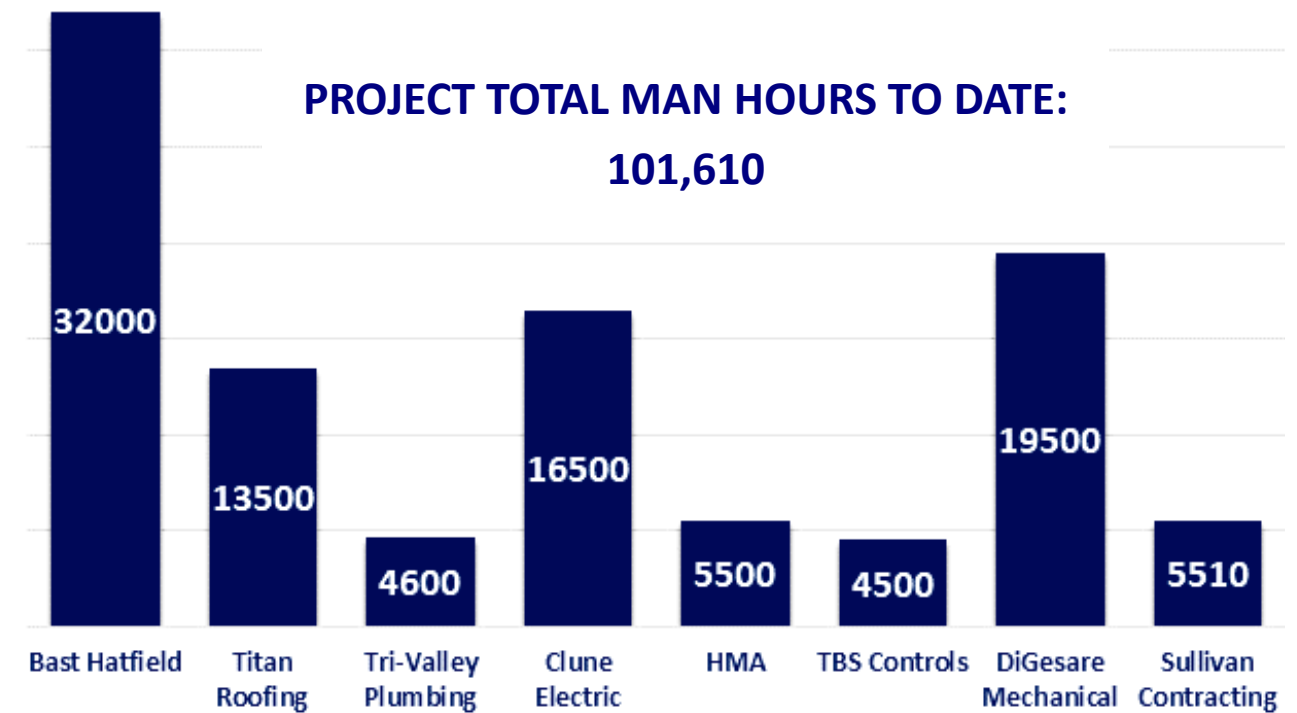

By Turner Construction

HS Site



ES SITE



ES SITE





AUDITORIUM



HS CAFETERIA



ES VESTIBULE



ES CAFETERIA

Turner
Construction Company



CS**ARCH**

ES CLASSROOM



HS CLASSROOM



HS ART ROOM



HOME & CAREERS





HS GYM



ES GYM



ES GYM



HS GYM
