

Schedule Milestones

Description	Original Start	Revised/ Actual	Original Completion	Revised/ Actual
Mobilize	5/28/2018	6/7/2018		
HS Site	5/28/2018	6/11/2018	9/30/2019	
POD K	7/2/2018	7/2/2018	12/28/2018	
POD B	7/2/2018	6/25/2018	1/20/2019	
POD I Multipurpose	6/25/2018	7/5/2018	8/17/2018	8/31/2018
POD J Addition	8/20/2018	9/4/2018	12/21/2018	
POD I Kitchen/Classrooms	12/24/2018		6/28/2019	
POD A	1/2/2019		6/28/2019	
POD G	1/2/2019		4/5/2019	
POD H	1/2/2019		4/5/2019	
POD D	4/8/2019		8/15/2019	
POD E	4/15/2019		9/13/2019	
POD F	4/15/2019		9/13/2019	
POD C	6/3/2019		8/23/2019	
POD J Classrooms	6/24/2019		8/30/2019	
ES Site	6/24/2019		8/30/2019	
Old Bus Garage Demo	6/4/2018	6/7/2018	7/27/2018	6/28/2018
Comments: Schedule Update 8/31/2018				

Engineering Status

Requests for Information			
Total RFIs	Closed RFIs	Open RFIs	Overdue RFIs
82	77	5	3
Submittals			
Open Items	Closed Items	In Review	Overdue
427	238	34	0
TOTAL:	699	% Closed:	34%



Contractor Billings

Previous Billings	Current Billing	Total to Date
July 2018	August 2018	Thru August 2018
\$1,606,823.09	\$2,602,020.12	\$4,795,722.16

Field Reports / Inspections

Inspections performed	Date Issued	Status
Dente Group—SWPPP	On-Going	Weekly
PSI—Air Monitoring	On-Going	As Necessary

Prime Contractors:

- 1) Sullivan Contracting—Abatement Contractor (AC)
- 2) HMA Contracting—Site Contractor (SC)
- 3) Bast Hatfield Construction —General Contractor (GC)
- 4) DiGesare Mechanical—Mechanical Contractor (MC)
- 5) Clune Electric—Electrical Contractor (EC)
- 6) Tri-Valley Plumbing —Plumbing Contractor (PC)
- 7) Titan Roofing—Roofing Contractor (RC)
- 8) TBS Controls—Controls Contractor (CC)

Project Update:

- ⇒ Abatement completed in 85% of entire school.
- ⇒ Roofing Work Progressing: 70% Complete.
- ⇒ High School Site Work progressing:

◆ Main parking lot has been paved with binder and turned over to the district for the school year.

◆ Sidewalks installed around main parking lot

◆ Maintenance parking lot/part of maintenance road paved

◆ Underground storm system installed for new tennis courts

◆ Continued site lighting installation
- ⇒ New parking spaces added at Bus Garage.
- ⇒ POD K work progressing:

◆ POD K ES Gym mudded pipe fittings abated

◆ Temporary partitions installed

◆ Interior demolition of entire space 95% complete

◆ Bathroom demolition includes demolishing and rerouting of underground plumbing piping

◆ Installation of new mechanical/plumbing piping

◆ Installation of new electrical wiring/equipment
- ⇒ POD B Work progressing:

◆ Temporary partitions installed

◆ Interior demolition of entire space 90% complete

◆ Part of stage floor demolished to prepare for new flooring

◆ ADA Viewing Platforms installed in Auditorium

◆ Installation of new mechanical piping/ductwork

◆ Installation of new electrical wiring/equipment
- ⇒ POD I Multipurpose Room/Pantry Work Progressing:

◆ Steel mezzanine installed—>Mechanical Unit Installed

◆ New ceiling installed

◆ Renovated and Enlarged Pantry Space

◆ Multipurpose room painted


◆ Installation of lights & new electrical wiring/equipment

◆ Installation of new ductwork and mechanical equipment
- ⇒ POD I Classrooms installation of new VCT Flooring.
- We look forward to the on-going work throughout the school year and continuing to build on our positive relationship with the district.

New HS Main Parking Lot \*Binder Only\*



HS New Canopy Sidewalk and Asphalt

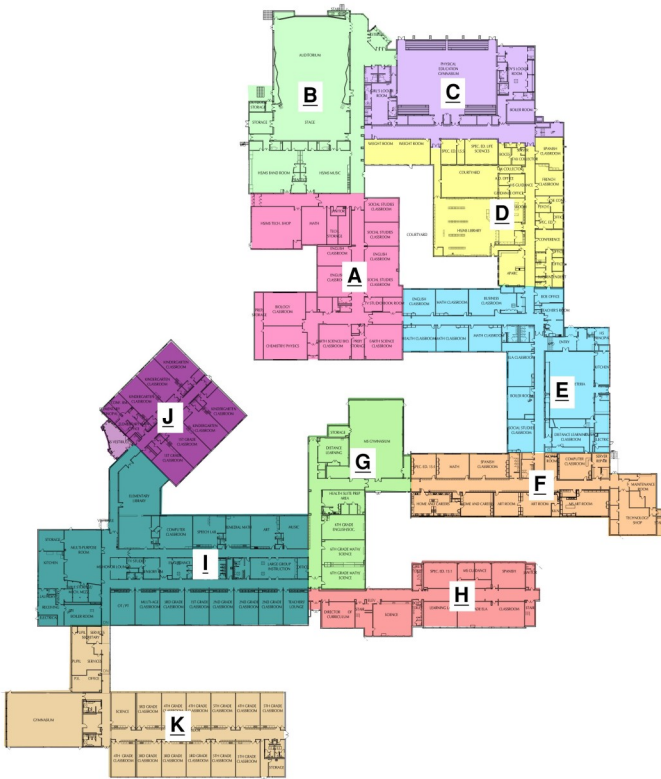




**Galway CSD Capital Improvement Project  
Executive Summary August 2018**

POD H New Roof Installation



POD J New Roof Installation

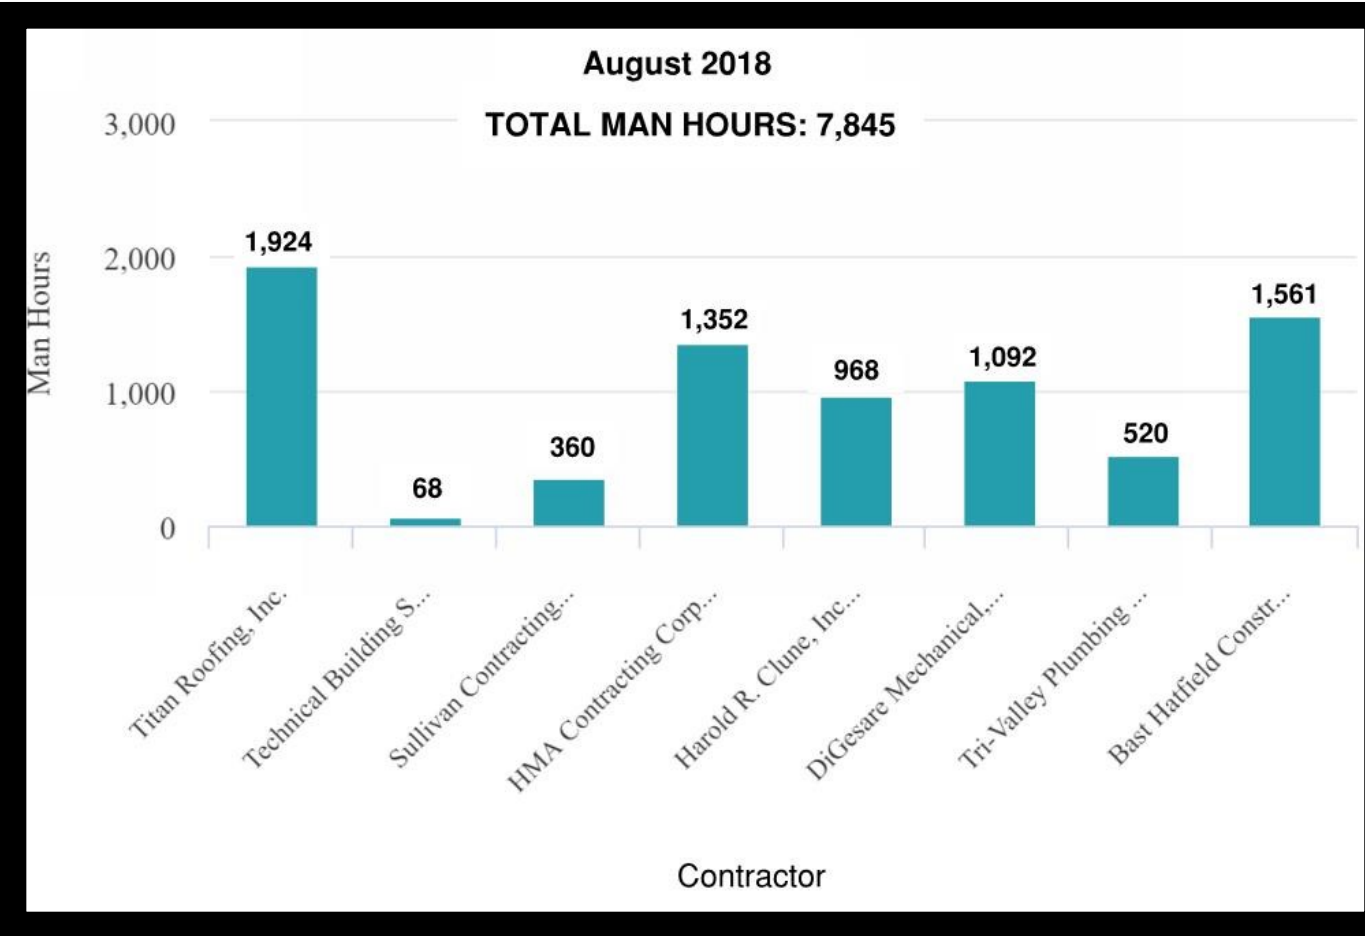

HS Storm System Installation Student Parking Lot



POD I New Mechanical Steel Mezzanine



POD I Newly Installed Classroom Floors



POD I New ES Cafeteria Final Touches
